

新北環狀線秀朗橋站土地開發捷運聯開辦公大樓案新建工程 (建照號碼：111中建字第118號)



工程進度說明



新北市政府捷運工程局



冠德建設股份有限公司



根基營造股份有限公司



李祖原聯合建築師事務所

建管說明

建管作業		
申報階段	預定申報	實際申報
施工計劃	111-06-15	111-06-15
開工申報	111-07-13	111-07-13
放樣勘驗	111-09-02	111-09-02
7FL勘驗	112-03-07	112-03-07
8FL勘驗	112-04-06	112-04-06
9FL勘驗	112-04-28	112-04-28
10FL勘驗	112-05-19	112-05-19
11FL勘驗	112-06-15	112-06-14
12FL勘驗	112-07-09	112-07-12
13FL勘驗	112-08-02	112-08-04
14FL勘驗	112-08-25	112-08-31
15FL勘驗	112-09-15	112-09-25
16FL勘驗	112-10-06	
17FL勘驗	112-11-03	
18FL勘驗	112-11-28	
19FL勘驗	112-12-21	
20FL勘驗	113-01-14	
屋頂板勘驗	113-02-03	
竣勘送件	113-07-04	
使照送件	113-07-15	


品質管制-鋼筋材料試驗



拉伸試驗



彎曲試驗

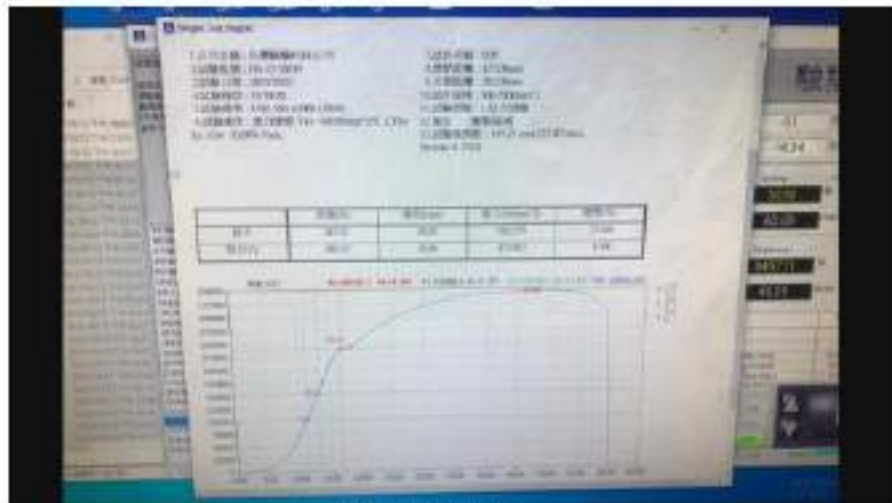

試驗數值



試驗結果

其他事項-安全衛生及敦親睦鄰



敦親睦鄰環境清潔



捷運機房清潔



捷運露台清潔



安全母索設置

施工照片



植筋



模板組立



灑水配管




放樣

施工照片-工地空拍照片



上週(112/10/07)

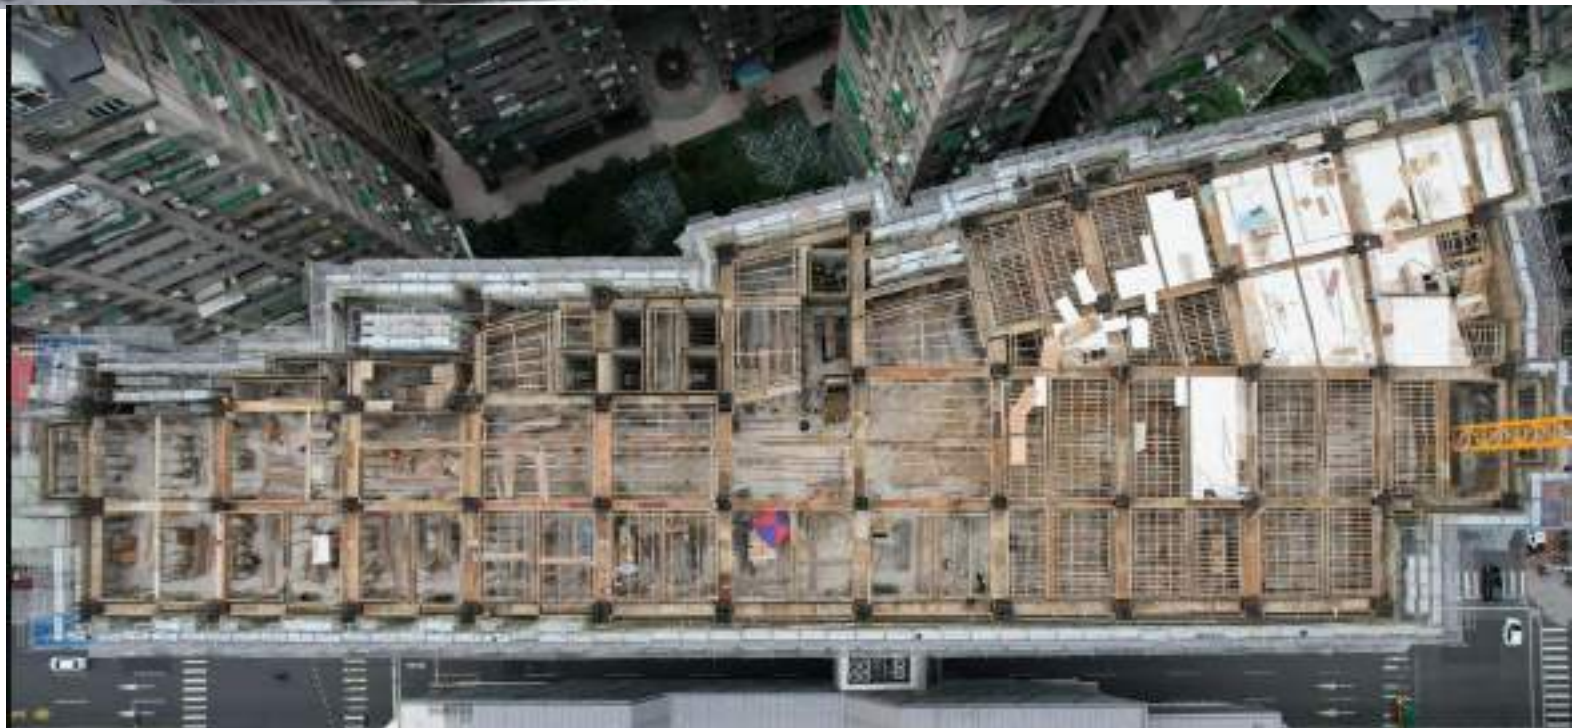

本週(112/10/13)
